


# OCTOBER 2009 DRILL RESULTS (MAIN ZONE NORTH)

## PLAN VIEW - DRILL HOLES PROJECTED TO PLANE

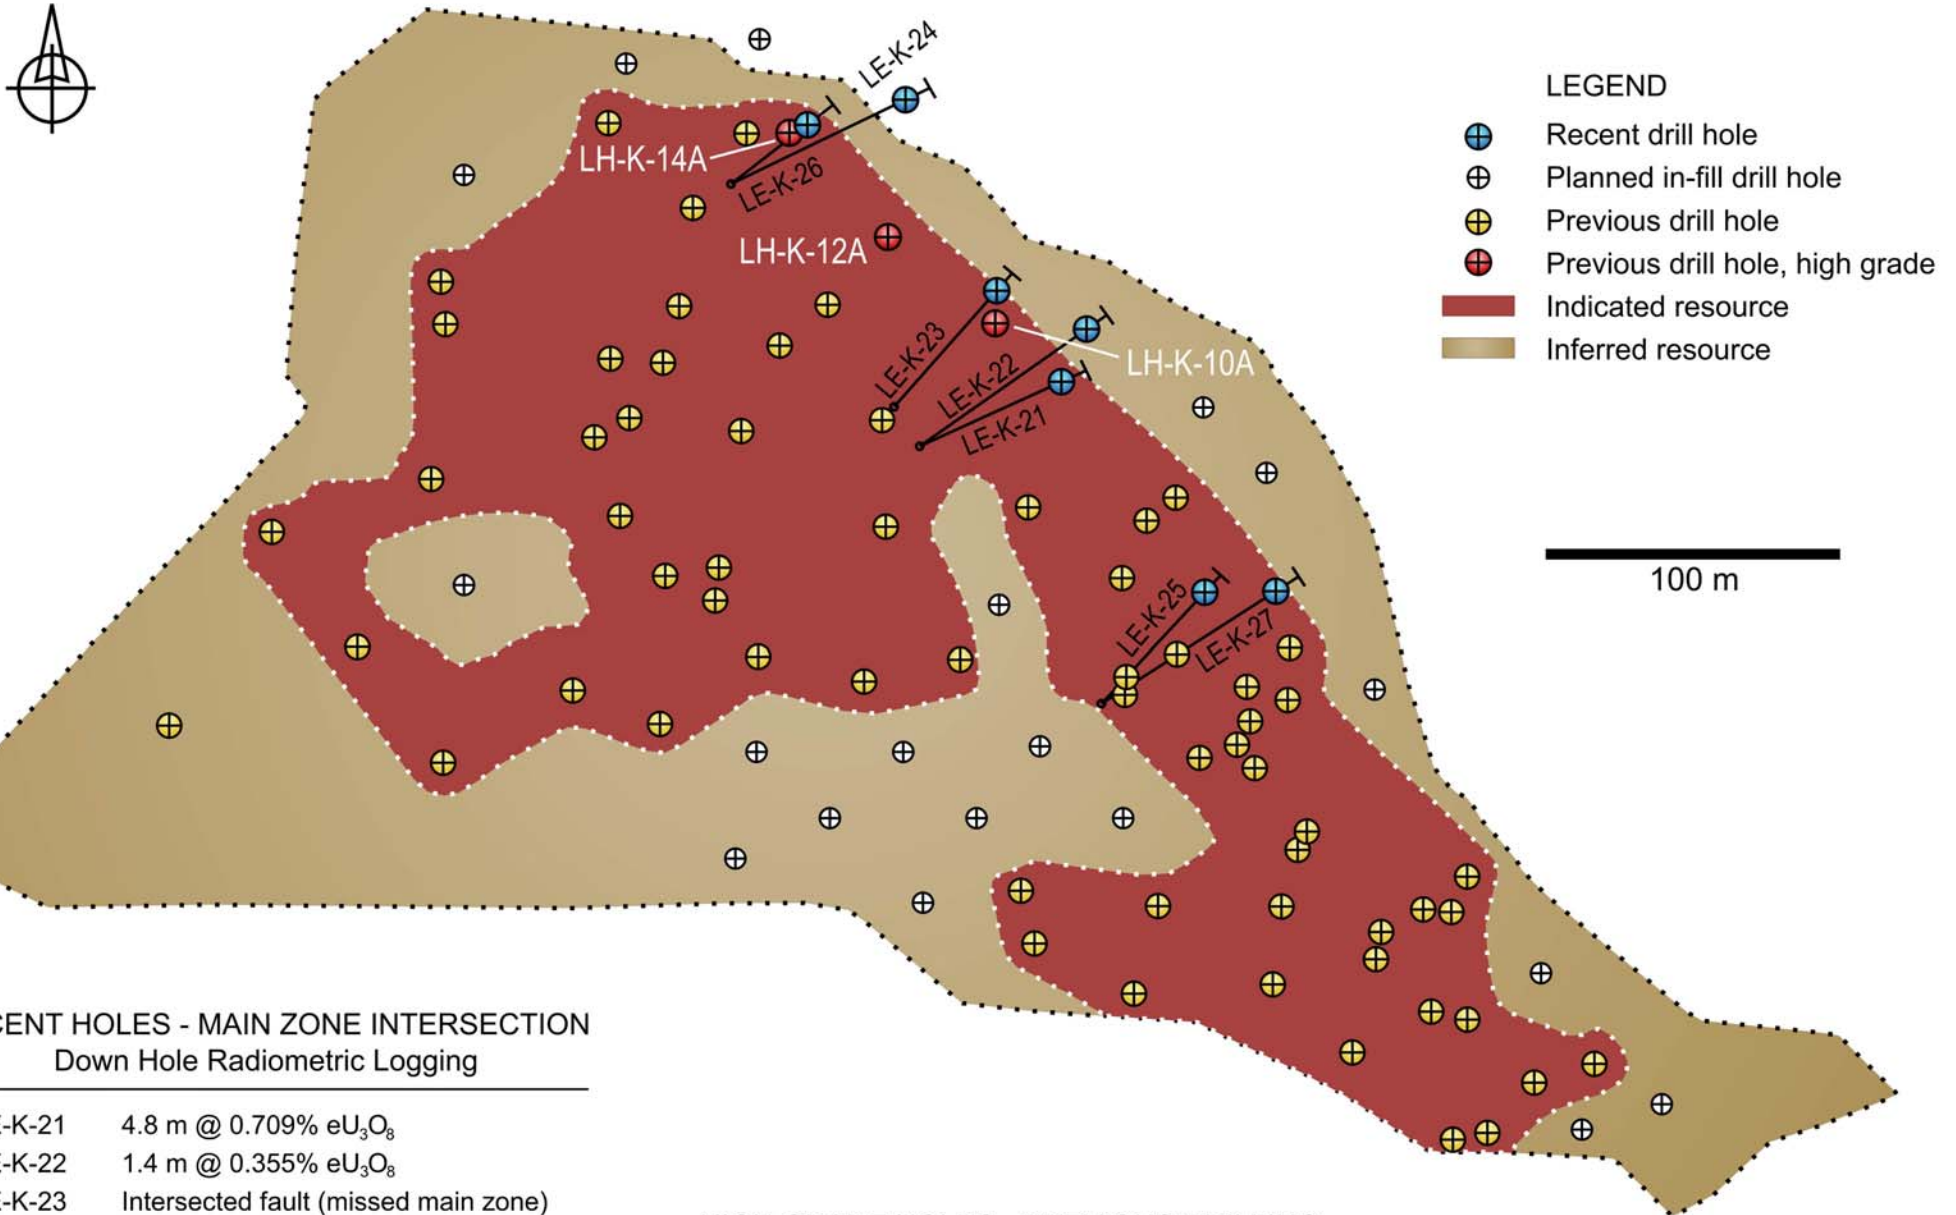

### RECENT HOLES - MAIN ZONE INTERSECTION

Down Hole Radiometric Logging

LE-K-21	4.8 m @ 0.709% eU <sub>3</sub> O <sub>8</sub>
LE-K-22	1.4 m @ 0.355% eU <sub>3</sub> O <sub>8</sub>
LE-K-23	Intersected fault (missed main zone)
LE-K-24	1.8 m @ 0.625% eU <sub>3</sub> O <sub>8</sub>
LE-K-25	1.2 m @ 0.471% eU <sub>3</sub> O <sub>8</sub>
LE-K-26	3.7 m @ 0.421% eU <sub>3</sub> O <sub>8</sub>
LE-K-27	2.0 m @ 0.761% eU <sub>3</sub> O <sub>8</sub>
	2.0 m @ 0.644% eU <sub>3</sub> O <sub>8</sub>

### HIGH GRADE HOLES - PREVIOUS DRILLING

Chemical Assay

LH-K-14A	6.0 m @ 0.79% U <sub>3</sub> O <sub>8</sub>
LH-K-12A	2.35 m @ 1.38% U <sub>3</sub> O <sub>8</sub>
LH-K-10A	6.5 m @ 2.16% U <sub>3</sub> O <sub>8</sub>
